




July 2017 HDHQ Construction Small Business Dashboard

Summary


These charts are based on contracts awarded through July 2017.

The contractor's goal is to award 20% of total contract dollars to MWSDVESB firms. Currently, the MWSDVESB Contracted is 9.2% and the MWSDVESB Paid is 0.2%.


HDHQ MWSDVESB Firms Ethnicity

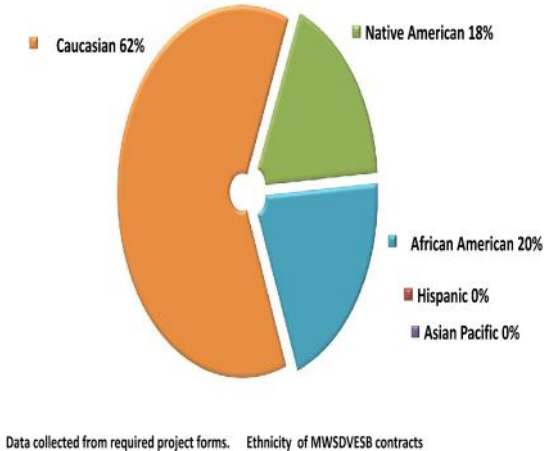


HDHQ Total Construction Contracts Awarded

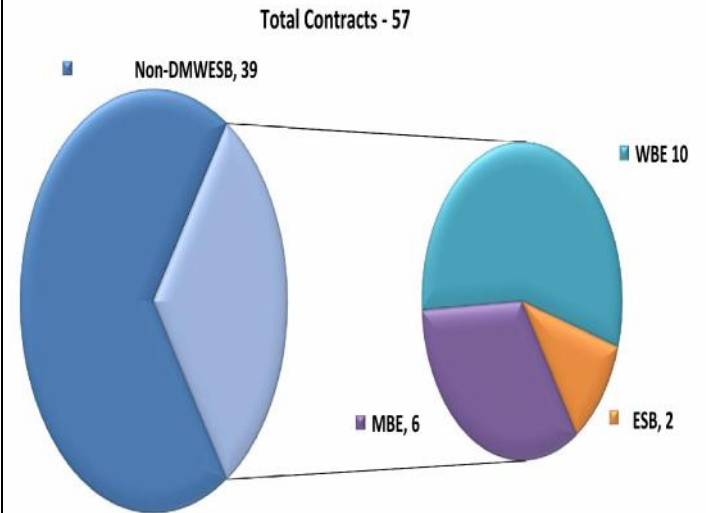

Multnomah County Health Department Headquarters Construction MWSDVESB Participation

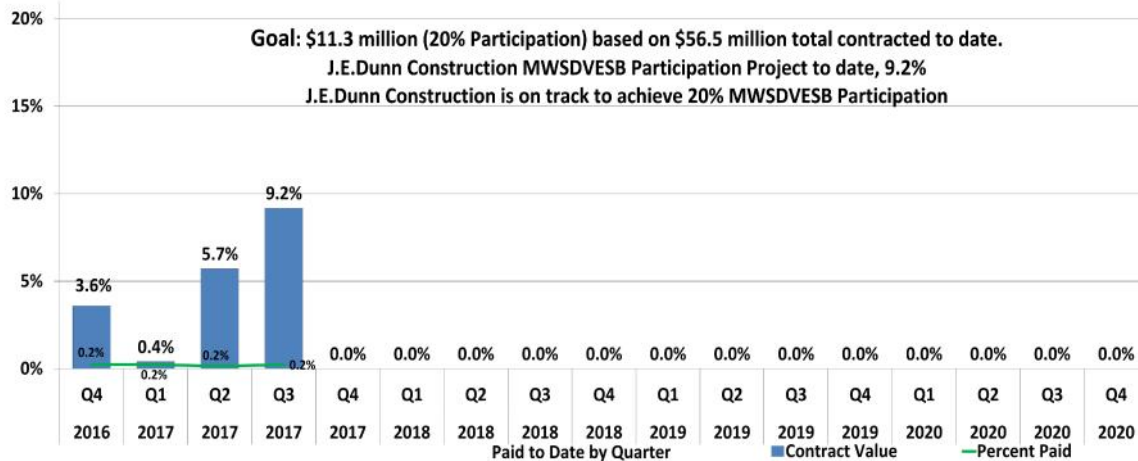

HDHQ MWSDVESB Participation by Dollars

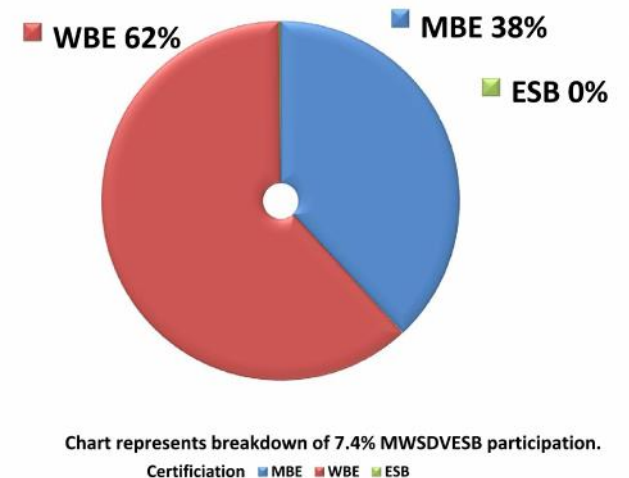

Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran


Cumulative Construction Data from 12/31/2016 to 7/31/2017. Produced by Group AGB, Ltd.



July 2017 HDHQ Construction Workforce Dashboard

Summary

-)] Total Project Apprenticeship to date is 22%
-)] Project Goal is 20% apprenticeship by trade
-)] Project minority participation is 20% and female is 17%

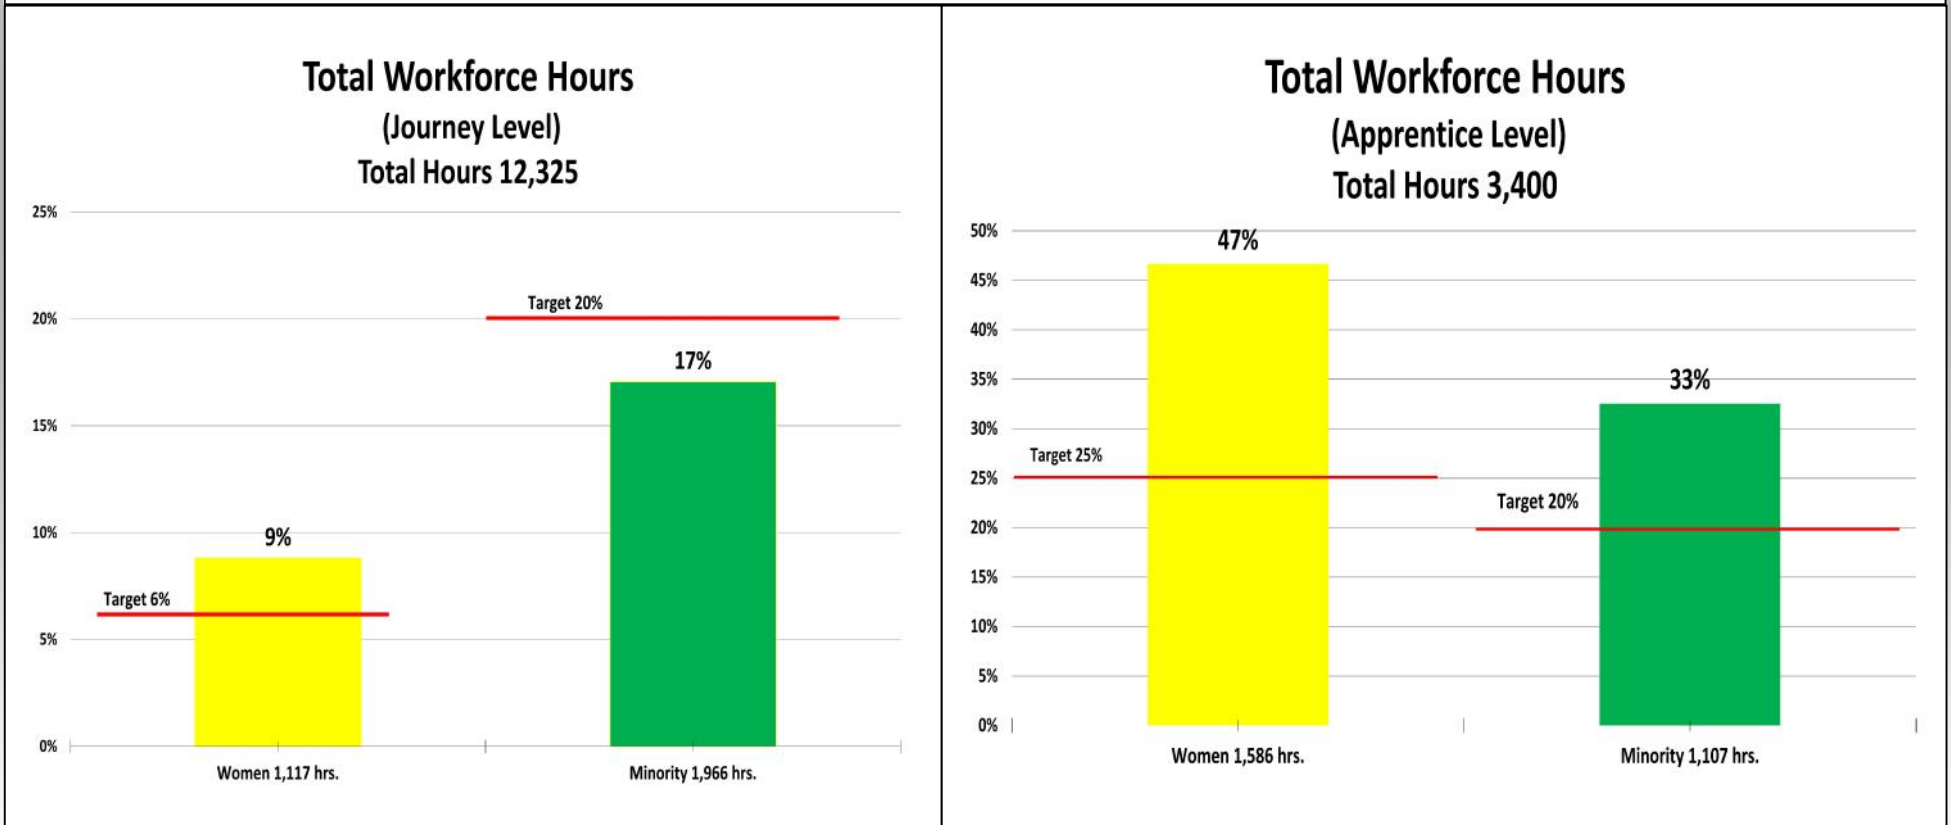


Cumulative Construction Data from 12/31/2016 to 7/31/2017
WTHP Participation for minorities and women for apprentices and journey level in accordance with the PLA.
Produced by Group AGB, Ltd.



July 2017 HDHQ Construction Workforce Dashboard

HDHQ Apprenticeship by Trade Goal 20% by trade

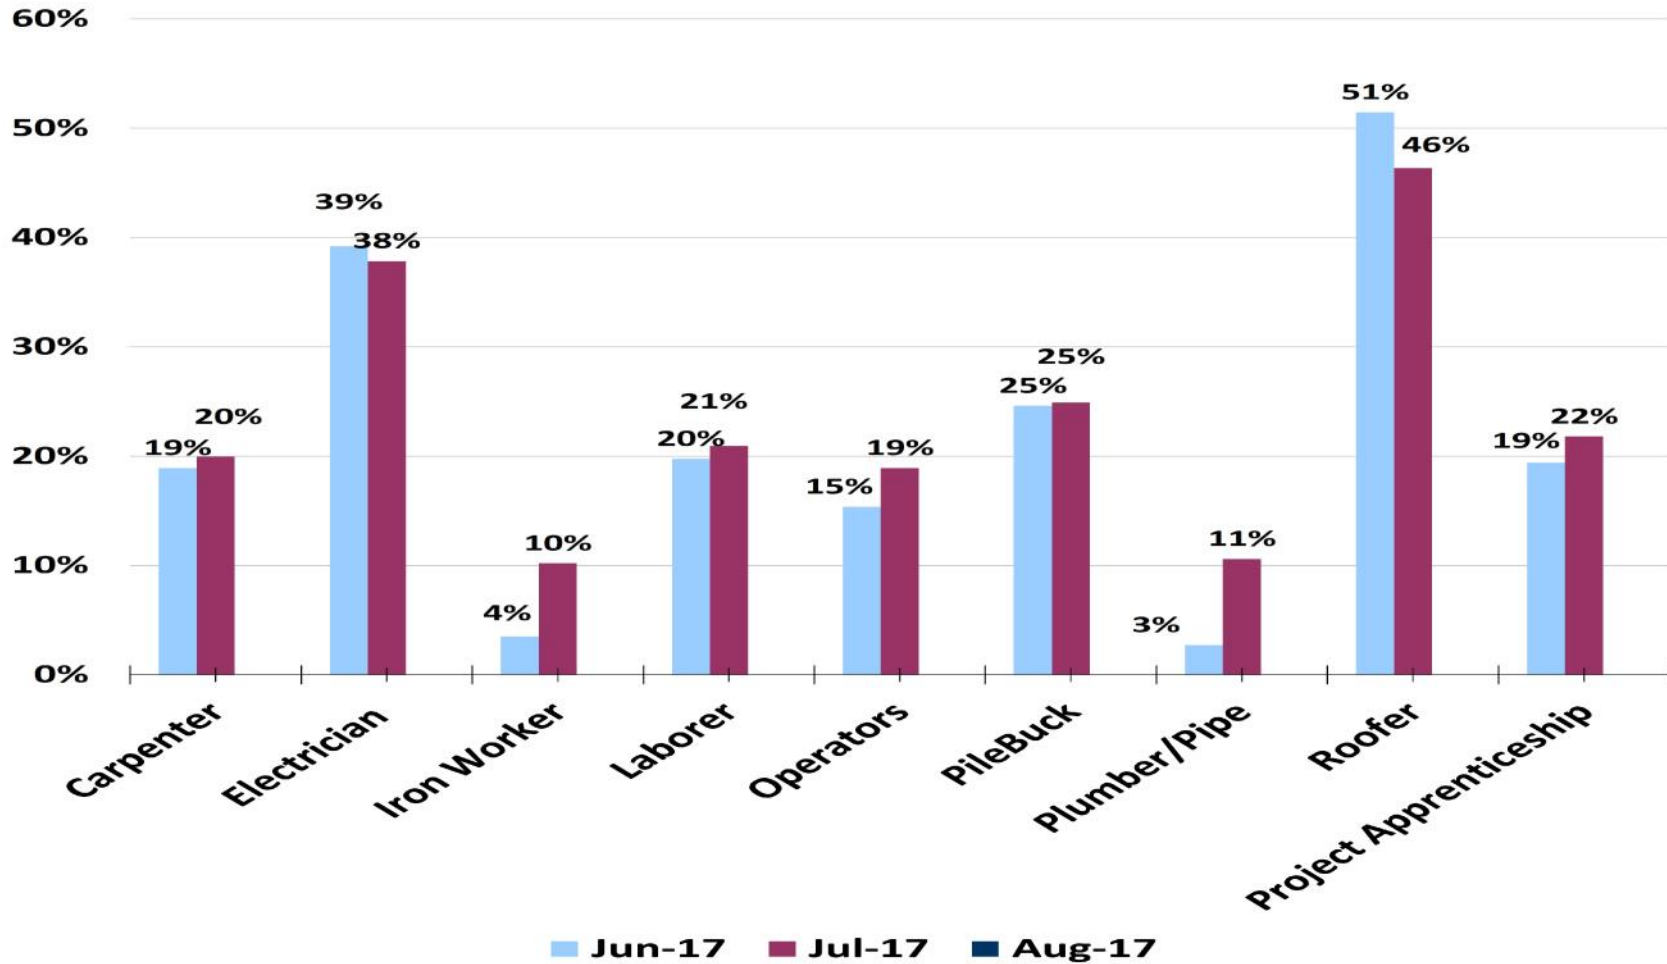

Cumulative Construction Data from 12/31/2016 to 7/31/2017
WTHP Participation of minorities and women for apprentices and journey level in accordance with the PLA.
Produced by Group AGB, Ltd.




July 2017 HDHQ Construction Workforce Dashboard

Summary

- HDHQ GMP of \$65,929,995 approved in June 2017
- MWSDVESB contracted and WFTH percentages represents mostly pre-construction and foundation work
- J.E.Dunn Construction is on track to achieve 20% MWSDVESB Participation
- Project exceeding female participation targets

Total Male Workforce Ethnicity

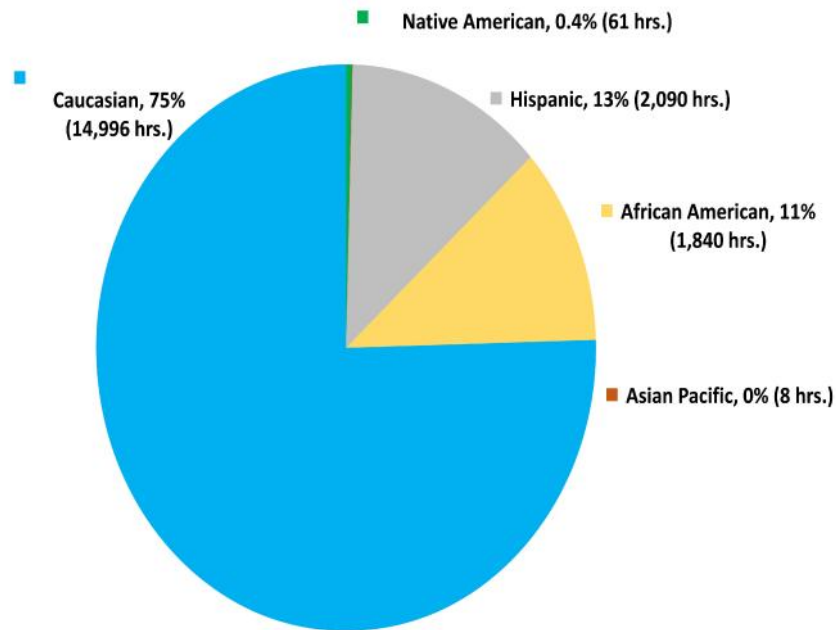

Total Female Workforce Ethnicity

